


# Barbers Hill ISD Bond 2017 Update


**Board Meeting: December 16, 2019** 





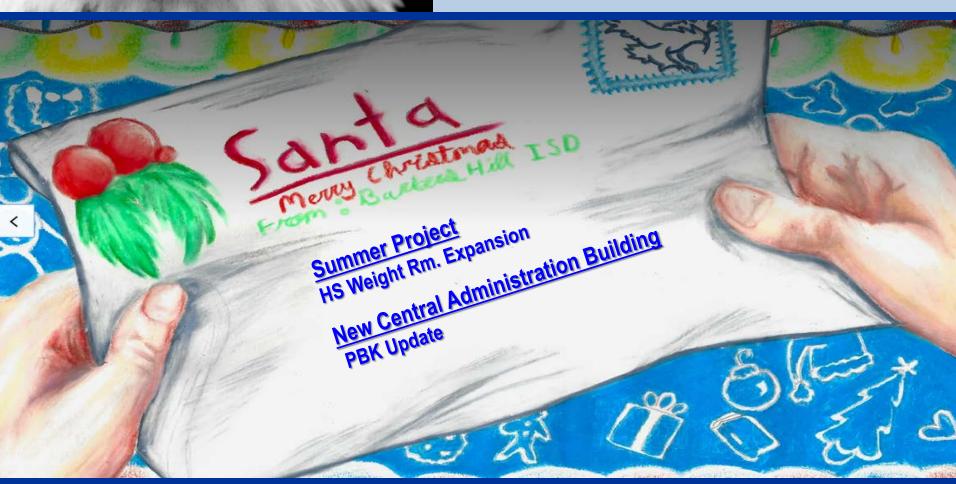



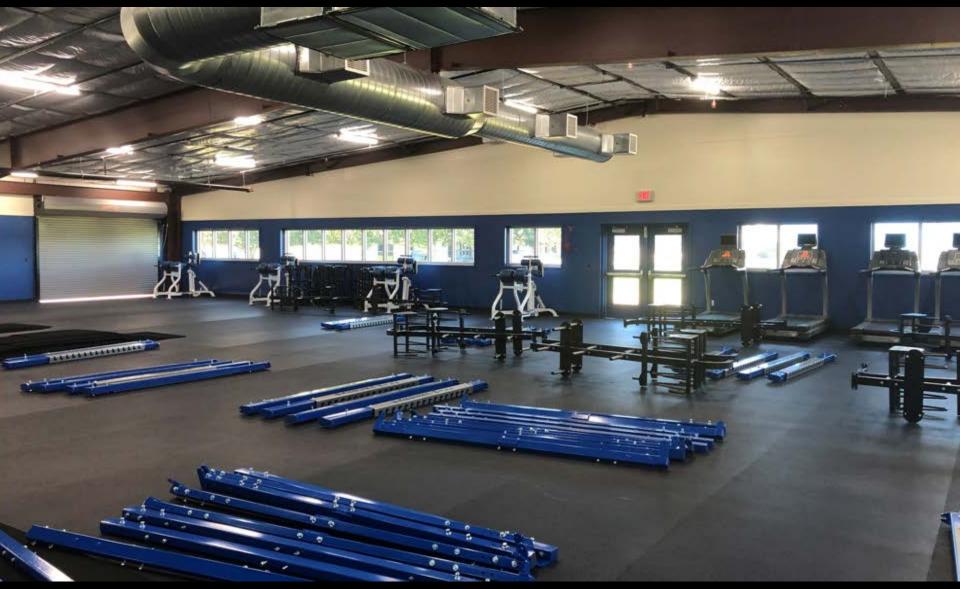

















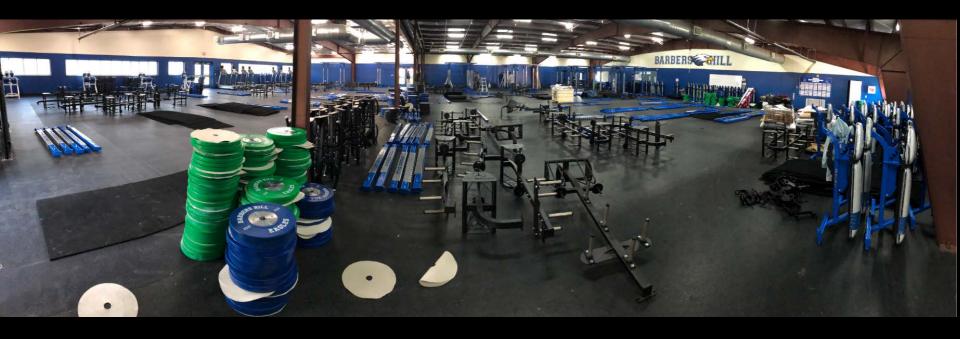





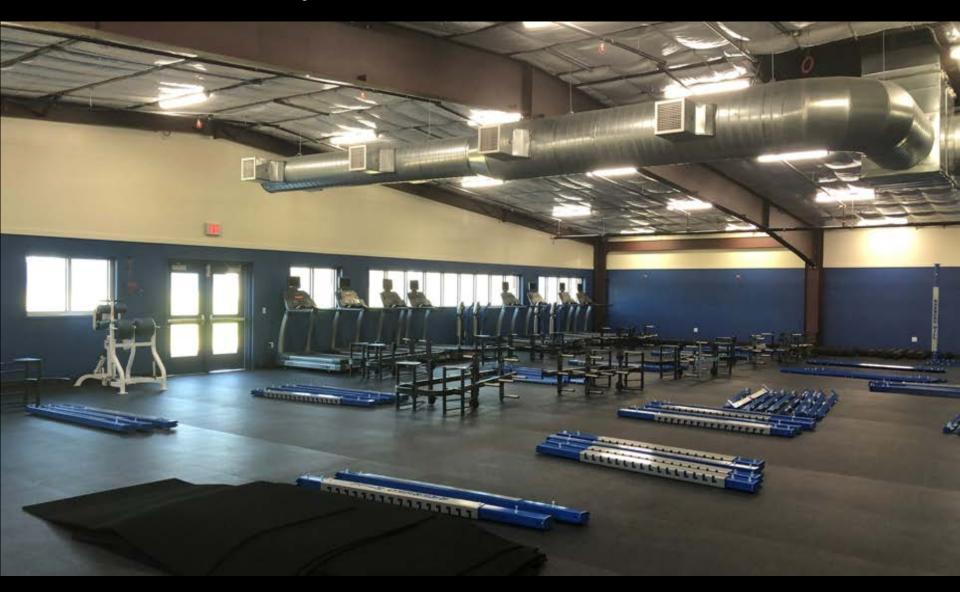







#### Bond 2017 - ADMINISTRATION BUILDING EARLY RELEASE PACKAGE 1 GMP








#### **Bond 2017 – ADMINISTRATION BUILDING**







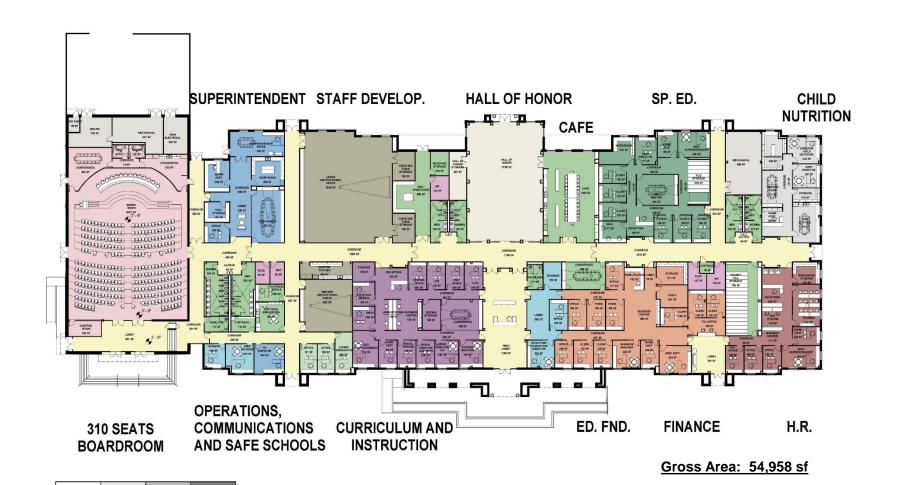











#### Schedule Update





<b>DESIGN DEVELOPMENT (DD) PHASE</b> September 16 – November 15, 2019	
<ul> <li>Final DD Presentation Submitted</li> </ul>	November 15, 2019
<ul> <li>PROPOSED SCOPE FREEZE</li> </ul>	November 15, 2019
<ul> <li>EXTENDED SCOPE FREEZE</li> </ul>	December 10, 2019
CONSTRUCTION DOCUMENT PHASE December 10, 2019 – April 6, 2020	
PACKAGE 1: Demolition, Earthwork, Building Pad, Civil Underground	
ISSUE FOR PROPOSAL	November 18, 2019
Recommend Award at BOT Meeting	December 16, 2019
❖ PACKAGE 2: Foundation, Structural Steel Purchase & MEP Under-slab	
■ ISSUE FOR PROPOSAL	January 27, 2020
Recommend Award at BOT Meeting	February 24, 2020
❖ PACKAGE 3: Building Package	
30% Construction Documents	January 13, 2020
60% Construction Documents	February 3, 2020
<ul> <li>90% Construction Documents / Issue For Permit</li> </ul>	March 6, 2020
<ul> <li>ISSUE FOR PROPOSAL</li> </ul>	
Recommend Award at BOT Meeting	May 18, 2020
· ·	
CONSTRUCTION ADMINISTRATION PHASE January 15, 2020 – July 15, 2021	
District vacate and salvage from ECC	
Mobilization	
■ Demolition + Package 1 Scope (2 months)January 15, 2020 – March 15, 2020	
■ Package 2 Scope (3 months)	
Package 3 Scope (13 months)	
Substantial Completion	





## **Board Room Finishes – Option "A"**










## **Board Room Finishes – Option "B"**

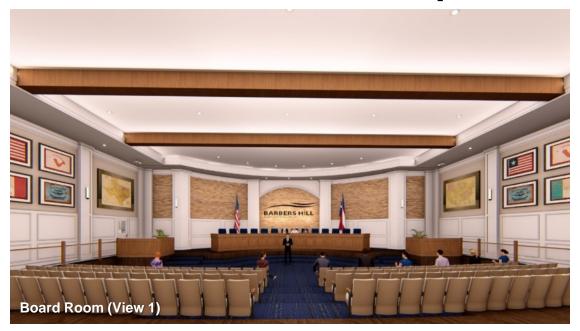







# **Board Room Finishes – Option "C"**









# **Board Room Finishes – Option "D"**























Independent School District

#### Bond 2017 - Early Childhood Center





# Thank You

